

Decker Island Phase II Progress Report

October 27, 2003

Construction Activities

Decker Island

- Contractor continues to shave off the top few feet on Decker Island and transport the material to Bradford.
- MBK has completed revisions of the Decker Island contours and will forward to DWR and DFG for review.

Bradford Island

- Contractor has off-loaded 11 barges to date. Approximately 36,000 tons (20,000 cy) of material has been placed on Bradford Island.
- Contractor has completed placing material at the levee toe from approximately Sta. 138+00 to 158+00.

Jersey Island

- No construction activities planned until mid November.

Van Sickle Island

- No construction activities planned until spring 2004.



Conveyor loading fill material onto barge.



Excavator loading fill material into hopper.

Decker Island Habitat Enhancement Project - 10/24/2003

Photographer - Don Trieu

MBK 
ENGINEERS



Excavator loading fill material onto hopper; silt fence to be installed at base of conveyor.



Conveyor loading material onto barge.

Decker Island Habitat Enhancement Project - 10/24/2003

Photographer - Don Trieu

MBK 
ENGINEERS



Fully loaded barge passing Three Mile Slough Bridge.




Water hyacinth collecting behind log boom at breach site.

Decker Island Habitat Enhancement Project - 10/24/2003

Photographer - Don Trieu

MBK 
ENGINEERS

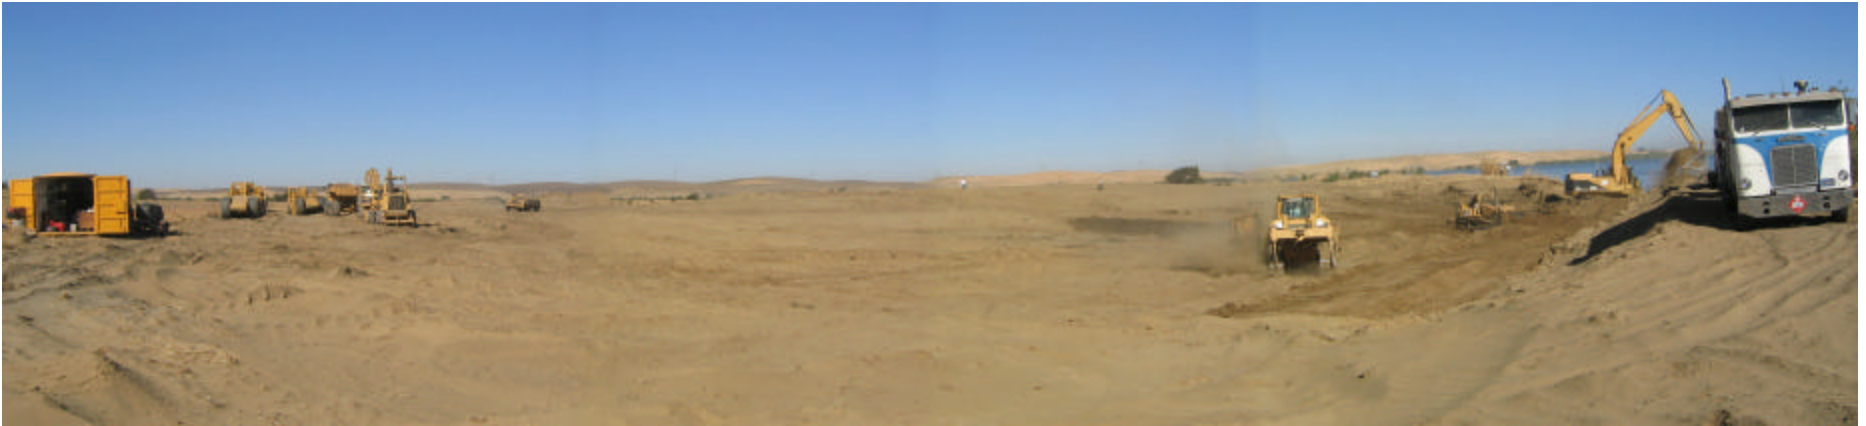

Looking north from the southeast corner of the DFG property.

Decker Island Habitat Enhancement Project – 10/27/2003

Photographer - Don Trieu

MBK 
ENGINEERS
